

GENERAL CONTRACTORS DAILY LOG

Company: Dragados
 Project: JWPCP Effluent Outfall Tunnel
 Location: JWPCP Site
 No. of Days Worked on Project: 1368

Date: 04/09/2024
 Weather: Sunny
 Site Conditions: Normal
 Temp: 76

Dragados Staff*	
Office Staff	1
Field Staff	2
Safety	1

Dragados Personnel	
Foreman	1
Operators	6
Laborers	8
Cr Operators	1
Mechanics	3
Oiler	1
Gas Tester	1
Surveyor	1

Subcontractors Onsite	
WA RASIC	0
TENSA	0
TEI	2
Sixense	0
Landmark	0
Guard	1
District	1
HK	0
Ballard	0

Dragados Production Details		Shift Start:	2:00 PM	Shift End:	10:00 PM
Description of Work Performed		TBM ADVANCE			
TBM/Tunnel/STP Advance: 4351, 4352*, 4353, 4354, 4355, 4356 Ring Build: 4351, 4352*, 4353, 4354, 4355, 4356 -Performed vacuum test on erector and segment hoist both passed. -Performed daily mechanical TBM checks. -Drilled grout ports 1 and 3. -Extended slurry at 4352, and all utilities. -R/R oil from oiler at T/S pump #2. -R/R oil from oiler at EP2 pump. -R/R oil from oiler at HBW pump. -Greased P1.5 bearing impeller/motor. -Checked oiler at P2.1. -Checked oil level and oiler at P1.5. -Checked oil level waste water pump. -Checked oil level dewatering pump. -Started moving the navigation laser forward. -Cleaned the building area throughout the night. -Repaired waste pump for filter press #3. -Cleaned wet silo for filter press #1 (ongoing). -Brought in 3 totes of polymer. -Tail Seal Grease average: 486mm per push (68% of a barrel). 50% 214/ 50% Alcohol 4351: 375.42 gallons, 4352: 410.98 gallons, 4353: 316.40 gallons, 4354: 297.2 gallons, 4355: 282.6 gallons, 4356: 338.8 gallons	START STA		218+34.16		
	END STA		218+63.65		
		SHIFT		DAILY TOTAL	
	ADVANCE	6		7	
	RINGS BUILT	6		7	
	PT THREADED	0		0	
	PT TENSIONED	0		0	
	PT GROUTED	0		0	
	TBM GREASE CONSUMPTION				
	Grease Station	Δ Filling Level (mm)		Weight (KG)	
	TSG 1	1490		528	
	TSG 2	1430		507	
	EP2	420		113	
	HBW	350		114	
	Equipment				
	No.		Description		
	2		Crane (Liebherr 8200, GRT 880)		
	1		Excavator (CAT 315)		
	1		2000 Gal Water Truck		
	1		Skidsteer (JD 331)		
1		Loader (CAT 966)			
1		Segment Forklift (Hyundai 250D-9)			
1		Telehandler (GEHL RS9-50)			
1		Manlift (Skyjack SJ63AJ)			
4		Multi Service Vehicles			
Subcontractors		Shift Start:	2:00 PM	Shift End:	10:00 PM
TEI- TBM Electrical		Equipment (Rental)			
		No.		Description	
		1		Telehandler 10,000Lb	
		1		Telehandler 6,000Lb	
Accidents					
Zero Accident & Zero Injuries					
Special Tests/Inspection					
Superintendent Signature					
Michael Leslie					
Additional Notes					

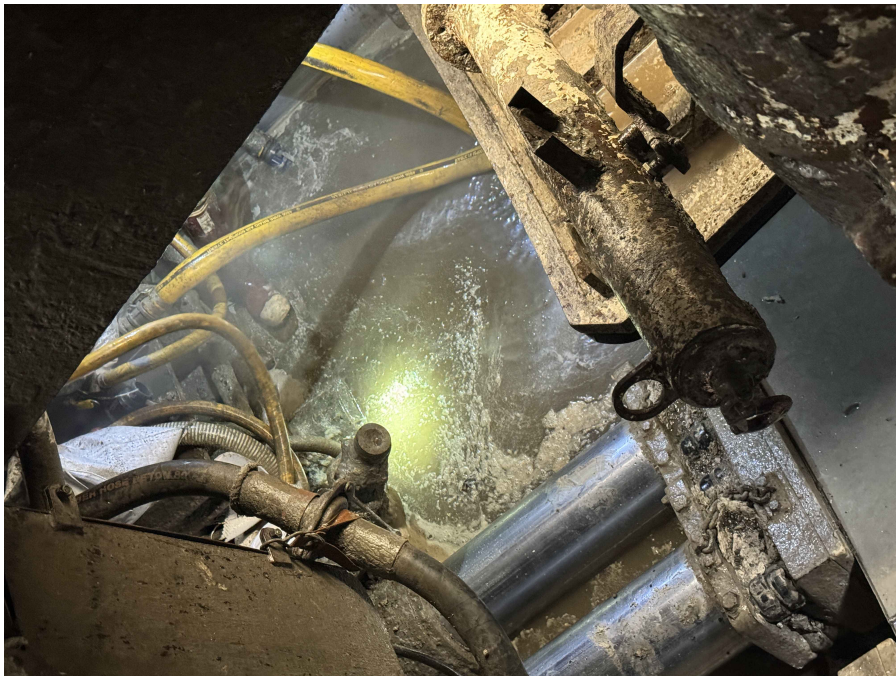


Image 1. Cleaning Out The Building Area Invert
